



East End Crossing Joint Board Construction Update August 20, 2014

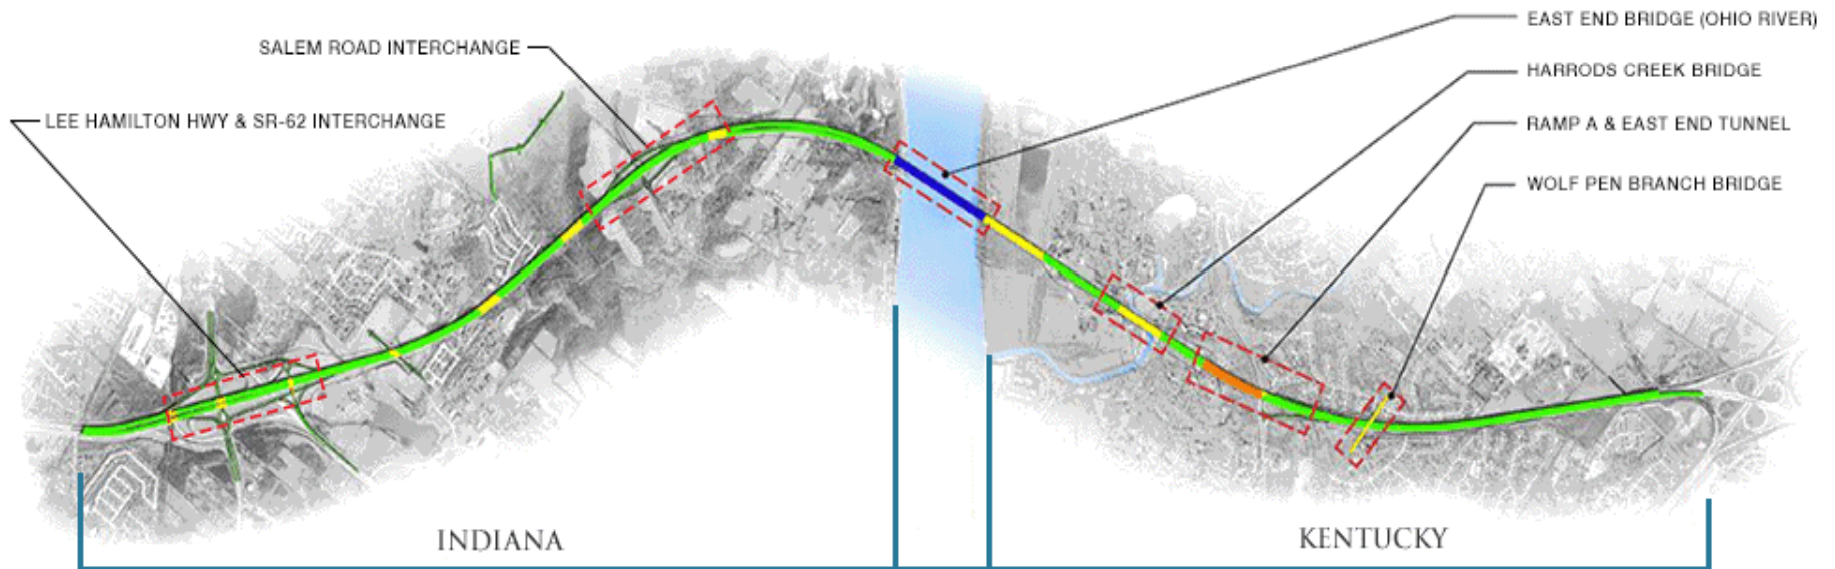

East End Construction – KY Approach


- Mass excavation along KY 841 from I-71 to US 42.
- Harrods Creek Bridge – Drilled shafts placed, working on columns and pier caps
- Approach Bridge – Working on multiple piers

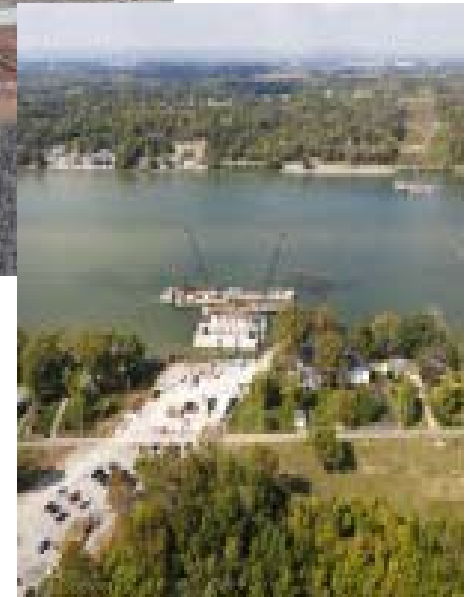

East End Construction – Tunnels



East End Construction – Main Span

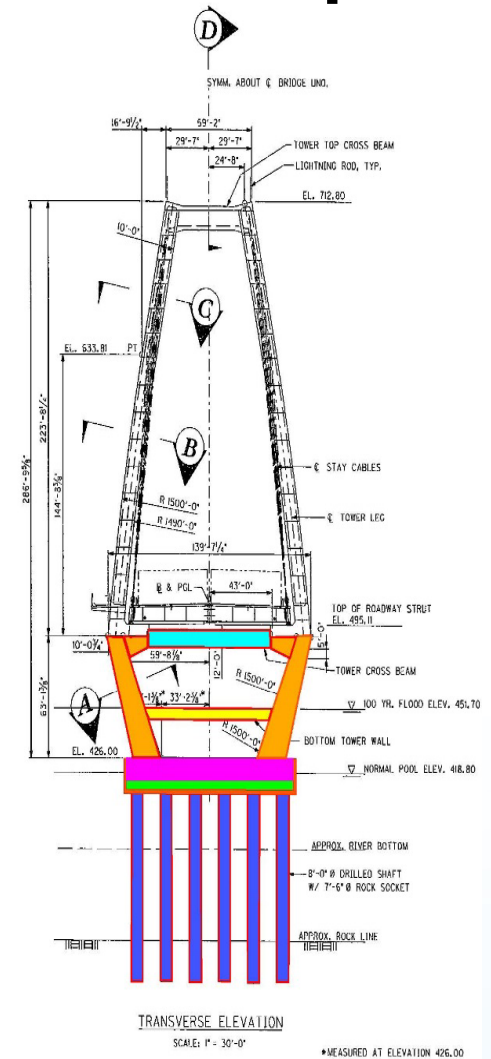

- Drilled Shafts Complete
- Waterline Foundations



East End Crossing – IN Approach

- Excavation and blasting from SR 62 to Ohio River
- Working on numerous bridge structures throughout section
- SR 265/SR 62 Interchange - Roundabouts



East End Crossing Construction - Summary

- Work is progressing on all 3 sections of the EEC
- EEC is approximately 40% complete
- EEC is on schedule for completion by October 31, 2016

